## report to **Board of Trustees**

### **Construction Projects Status Report**

Date March 18, 2025

Meeting Type Regular Meeting, Public Agenda

Tο **Board of Trustees** 

From Joanne Pitman

Chief Superintendent of Schools

Information Purpose

Originator Dany Breton, Superintendent, Facilities and Environmental Services

Governance

Policy Reference

Operational Expectations

OE-7: Communication With and Support for the Board

OE-9: Facilities

Resource Person(s) Trevor Fenton, Director, Facility Projects

David Jaimes, Project Manager, Facility Projects Colt Chesney, Project Manager, Facility Projects

#### 1 | Recommendation

This report is being provided for information to the Board of Trustees. No decision is required at this time.

#### 2 | Issue

The Chief Superintendent is required to provide the Board of Trustees with an update regarding the status of major capital projects including new schools, modernizations, additions and Modular Classroom Program (MCP) projects currently under development or construction.

The Calgary Board of Education (CBE) has received construction approval for two new schools and two modernizations, and design-only approval for two new schools and one modernization. Additionally, "planning" activities are approved for one new school, while "pre-planning" activities are approved for two modernizations.

On March 4, 2022, the Government of Alberta (GoA) announced the approval of a middle school for Evanston. On December 14, 2022, Alberta Infrastructure (AI) advised that Evanston middle school will be delivered via a design-build delivery method. The design-build contract was awarded in November 2023 and construction commenced on April 25, 2024.

On November 29, 2022, the Board of Trustees approved the closure of the Louise Dean Centre at Kensington School effective June 28, 2024 for the purpose of relocation to Jack James High School (JJHS). Modernization and expansion of JJHS was required to accommodate the Louise Dean program. The project reached substantial completion in October 2024 and the program has been fully relocated. With only minor deficiencies remaining this will be the last update provided for this project.

On March 1, 2023, the GoA announced the approval of "Design and Construction" funding for the modernization of John G. Diefenbaker High School. A pre-design report outlining findings from stakeholder engagement and consultant site reviews was issued in December 2023. On April 16, 2024, Alberta Education granted approval to extend project timelines to allow CBE to conduct additional planning activities to further evaluate the project scope prior to proceeding with design.

On March 1, 2024, the GoA announced approval of "Design and Construction" funding for a new elementary school in the community of Evanston and "Design" funding for a new elementary school in the community of Redstone and a new high school in the community of Cornerstone. On August 8, 2024, the GoA approved a capacity increase of the Cornerstone high school from 1,800 to 2,410 students. On December 3, 2024, the GoA approved a capacity increase of Redstone elementary from 600 to 890 students. Al commenced pre-design work on August 6, 2024 for Evanston elementary, October 7, 2024 for Redstone elementary and December 13, 2024 for Cornerstone high school. On February 15, 2025 the GoA announced construction approval for both Redstone elementary and Cornerstone high school.

On March 1, 2024, the GoA announced the approval of "Design" funding for the modernization of Annie Gale School starting in 2026. On September 18, 2024, Alberta Education announced that design funding was being provided immediately to accelerate the delivery timeline. The project is being managed by CBE, with consultant procurement activities ongoing.

On March 1, 2024, the GoA announced that "Planning" funding for a new middle school located in the community of Saddle Ridge would be provided in 2026. On September 26, 2024, Alberta Education announced that "Planning" funding was being provided immediately to accelerate the delivery timeline. Work is underway to conduct tasks associated with this project phase.



On March 1, 2023, the GoA announced the approval of "Pre-Planning" funding for modernizations at A.E. Cross School and Sir John A. MacDonald School. On February 7, 2024, funding approval was received for these projects. Work is underway through third party consulting firms to complete the necessary studies to help inform next steps.

The MCP provides school jurisdictions with new modular classrooms, modular/portable unit relocations and demolitions to assist school jurisdictions with the accommodation of students on an urgent basis. On March 31, 2023, as a part of the 2023-24 MCP, Alberta Education provided approval for the relocation of five and the demolition of 11 modular classrooms. On March 14, 2024, as part of the 2024-25 MCP, Alberta Education approved 12 new and the relocation of six modular classrooms. On April 9, 2024, the CBE Board of Trustees approved the use of Capital Reserves to relocate six modular classrooms. On August 2, 2024, as a part of the 2024-25 MCP, Alberta Education provided in-year approval of an additional 35 new and the relocation of five modular classrooms. On August 26, 2024, due to the high enrolment pressures and at CBE's request, Alberta Education rescinded six of the previously approved modular demolitions from the 2023-24 MCP. In total, the CBE is currently in the process of delivering the addition of 47 new, relocation of 22 and demolition of 6 modular classrooms. A full breakdown and status update of all ongoing MCP projects is available in **Attachment I**.

### 4 | Analysis

Information on the status of the projects under development and being administered by the CBE and AI is provided in **Attachment I**.

The locations of the various new school, existing school and MCP capital projects under development are shown in **Attachment II**.

**Attachment III** provides a series of onsite photographs to visually convey the progress at Evanston middle.

There are four Project Steering Committees set up for the following projects:

- Evanston elementary;
- Redstone elementary;
- Cornerstone high school; and
- Annie Gale School Modernization

### 5 | Conclusion



This report provides the current update on the project status of new schools and school modernizations within the CBE, which are currently under development or construction.

It is provided to the Board of Trustees for informational purposes in compliance with Operational Expectation 7: Communication With and Support for the Board.

## JOANNE PITMAN CHIEF SUPERINTENDENT OF SCHOOLS

#### **ATTACHMENTS**

Attachment I: New/Modernized Facility Construction Status

Attachment II: Project Location Map
Attachment III: Construction Photos

#### GLOSSARY - Developed by the Board of Trustees

Board: Board of Trustees

Governance Culture: The Board defined its own work and how it will be carried out. These policies clearly state the expectations the Board has for individual and collective behaviour.

Board/Chief Superintendent Relationship: The Board defined in policy how authority is delegated to its only point of connection – the Chief Superintendent – and how the Chief Superintendent's performance will be evaluated.

Operational Expectations: These policies define both the nonnegotiable expectations and the clear boundaries within which the Chief Superintendent and staff must operate. They articulate the actions and decisions the Board would find either absolutely necessary or totally unacceptable.

Results: These are our statements of outcomes for each student in our district. The Results policies become the Chief Superintendent's and the organization's performance targets and form the basis for judging organization and Chief Superintendent's performance.



## CALGARY BOARD OF EDUCATION NEW & EXISTING SCHOOL CONSTRUCTION STATUS March 18, 2025

Building	Opening Date	Notes/Comments		
41. Evanston Middle School Grades 5-9* Capacity 900 students	TBD	Design Build – RFP Package (includes drawing package to 30% development and Performance Specifications)  Design-Build Contract Award  Design and Specifications  Construction Progress  Note: Project managed by Alberta Infrastructure. Design-buil mobilized to site in late April 2024. Structural steel and maso progress, building envelope started.		
42. Louise Dean Centre Relocation Grades 9-12	Fall 2024	Design and Specifications Construction Award Construction Progress Note: Project managed by Calgary Board of Education. Prog to new site and operational as of October 15, 2024. Work ongoing to address minor deficiencies.	100% 100% 99% ram relocated	
43. John G. Diefenbaker School Grades 10-12 Modernization	TBD	Planning Phase  Note: Project managed by Alberta Infrastructure. Approved of budget of \$33.1M plus \$2.5M for HAZMAT abatement. Review underway for determination of next steps.		
44. Annie Gale School Grades 6-9 Modernization	TBD	Design and Specifications  Note: Project being managed by Calgary Board of Education approval received on September 18, 2024. Procurement for consultant ongoing.		
45. Cornerstone High School Grades 10-12* Capacity 2,400 students	TBD	Design and Specifications  Note: Design approval was announced on March 1, 2024. Co approval announced on February 15, 2025. Project manage Infrastructure. Internal engagement is ongoing. Design mee December 2024.	d by Alberta	
46. A.E. Cross School Grades 7-9 Modernization	TBD	Pre-Planning Phase  Note: Pre- Planning approved on March 1, 2023. Funding ap on February 7, 2024. Facility condition assessment nearing of	•	

Prepared by FES Page 1 of 6

<sup>\*</sup>Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.

## CALGARY BOARD OF EDUCATION NEW & EXISTING SCHOOL CONSTRUCTION STATUS March 18, 2025

Building	Opening Date	Notes/Comments		
47. Sir John A. MacDonald School Grades 6-9 Modernization	TBD	Pre-Planning Phase  Note: Pre-Planning approved on March 1, 2023 and funding received on February 7, 2024. Due to possible synergies, pre-planning activities were conducted and analyzed concurrently with the additional planning work to support the John G. Diefenbaker HS modernization project. Facility condition assessment nearing completion.		
48. Saddle Ridge Middle School Grades 5-9* Capacity 900 students	TBD	Planning Phase 25%  Note: Pre-Planning approved on March 1, 2023 and funding received on February 7, 2024. Project was advanced to Planning phase following a government announcement on March 1, 2024. Planning activities ongoing.		
49. Evanston Elementary School Grades K-4* Capacity 600 students	TBD	Design and Specifications  Construction Award  Construction Progress  Note: Project announced for design and construction on March 1, 2024.  Internal feedback gathering ongoing. Schematic design completed in January 2025. Design development currently underway.		
50. Redstone Elementary School Grades K-4* Capacity 600 students	TBD	Design and Specifications  Note: Project announced as design-only on March 1, 2024. Construction approval announced on February 15, 2025. Internal feedback gathering ongoing. Schematic design activities are currently underway.		

Prepared by FES Page 2 of 6

<sup>\*</sup>Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.

### CALGARY BOARD OF EDUCATION MODULAR CLASSROOM PROGRAM STATUS March 18, 2025

March 18, 2025 				
Building	Number Type of Units	Opening Date	Notes/Comments	
m1. Simons Valley School	4 Relocation	Fall 2024	Design and Specifications	100%
Grades K-6	4 Nelocation	1 all 2024	Construction Award	100%
Added Capacity: 100			Construction Progress	99%
			Note: Approved on March 31, 2023. Cons complete, partial occupancy granted late to ongoing to address remaining deficiencies deficiencies to be addressed in Spring 2020.	November 2024. Worl and seasonal
m? Jan Razalgotto School	1 Relocation	Fall 2024	Design and Specifications	100%
n2. lan Bazalgette School Grades 7-9	i Reiocation	ra11 2024	Construction Award	100%
Added Capacity: 25			Construction Progress	99%
ladou oupdoky. 20			Note: Approved on March 31, 2023. Construction activities complete, partial occupancy granted late November 2024. Wor ongoing to address deficiencies and seasonal deficiencies to b addressed in Spring 2025.	
m3. Colonel Walker School Grades K-6	1 Demolition	Fall 2024	Design and Specifications Construction Award	100%
Reduced Capacity: 25			Construction Progress	100%
,			Note: Approved on March 31, 2023. Cons complete. Deficiencies complete. This is t project.	
n4. WO Mitchell School	2 Demolition	Fall 2024	Design and Specifications	100%
Grades K-5		-	Construction Award	100%
Reduced Capacity: 50			Construction Progress	100%
			Note: Approved on March 31, 2023. Cons complete. Deficiencies complete. This is t project.	
m5. Sam Livingston School	1 Demolition	Fall 2024	Design and Specifications	100%
Grades K-4	i Demolition	1 all 2024	Construction Award	100%
Reduced Capacity: 25			Construction Progress	100%
The state of the s			Note: Approved on March 31, 2023. Conscomplete. Deficiencies complete. This is t project.	truction activities are

<sup>\*</sup>Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.

Prepared by FES Page 3 of 6

## CALGARY BOARD OF EDUCATION MODULAR CLASSROOM PROGRAM STATUS March 18, 2025

Building	Numbe of Uni	er Type ts	Opening Date	Notes/Comments		
n6. Battalion Park School	1	Demolition	Fall 2024	Design and Specifications	100%	
Grades K-6	•			Construction Award	100%	
Reduced Capacity: 25				Construction Progress	100%	
todacoa capasity. 20				Note: Approved on March 31, 2023. Construction complete. Deficiencies complete. This is the	ruction activities are	
			l	project.		
m7. Connaught School	4	New	Winter	Design and Specifications	100%	
Grades K-6	2	Relocation	2025	Construction Award	100%	
Added Capacity: 150				Construction Progress	5%	
				Note: Four new modulars approved on March 14, 2024 and two relocated modulars approved on April 9, 2024. Design complete Construction contracts finalized. Construction activities underward		
n8. Nelson Mandela HS	6	New	Winter	Design and Specifications	100%	
Grades 10-12			2025	Construction Award	100%	
Added Capacity: 150				Construction Progress	10%	
				Note: Approved on March 14, 2024. Design Construction contracts finalized. Construct		
n9. Prairie Sky School	3+1	New	Winter	Design and Specifications	100%	
Grades K-9	4	Relocation	2025	Construction Award	100%	
Added Capacity: 175				Construction Progress	5%	
				Note: Four relocated modulars approved o	n April 9, 2024 and	
				three new modular classrooms plus one ne approved on August 2, 2024. Design comp contracts finalized. Construction activities	ew modular washroor plete. Construction	
m10. Peter Lougheed School	4	4 New	Winter	Design and Specifications	100%	
Grades 5-9			2025	Construction Award	100%	
Added Capacity: 100				Construction Progress	10%	
				Note: Two new modulars approved on Mar new modulars approved on August 2, 2024 Construction contracts finalized. Construct	1. Design complete.	
	6	6 Relocation F	Fall 2024	Design and Specifications	100%	
n11. Sir Winston Churchill HS			0_ 1	•		
m11. Sir Winston Churchill HS Grades 10-12			ļ	Construction Award	100%	

<sup>\*</sup>Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.

Prepared by FES Page 4 of 6

### CALGARY BOARD OF EDUCATION MODULAR CLASSROOM PROGRAM STATUS March 18, 2025

m12. Joane Cardinal- Schubert HS Grades 10-12			Date			
				granted early December 2024. Work ongoing to address remaining deficiencies and seasonal deficiencies to be address in Spring 2025.		
Grades 10-12	5	Relocation	Spring	Design and Specifications	100%	
	1	New	2025	Construction Award	75%	
Added Capacity: 150				Construction Progress	0%	
				Note: Approved on August 2, 2024. Design is complete. Construction contracts are being finalized.		
m13. Mahogany School	4	New	Spring	Design and Specifications	100%	
Grades K-5			2025	Construction Award	75%	
Added Capacity: 100				Construction Progress	0%	
				Note: Approved on August 2, 2024. Design complete. Construction contracts are being finalized.		
m14. North Trail HS	6	New	Spring	Design and Specifications	100%	
Grades 10-12			2025	Construction Award	75%	
Added Capacity: 150			Construction Progress	0%		
				Note: Approved on August 2, 2024. Desig Construction contracts are being finalized		
m15. Hugh A. Bennett School	4	New	Spring	Design and Specifications	100%	
Grades K-4			2025	Construction Award	75%	
Added Capacity: 100				Construction Progress	0%	
				Note: Approved on August 2, 2024. Desig Construction contracts are being finalized	· · · · · · · · · · · · · · · · · · ·	
m16. Grant MacEwan School	6	New	Summer	Design and Specifications	100%	
Grades K-6			2025	Construction Award	50%	
Added Capacity: 150				Construction Progress	0%	
' '				Note: Approved on August 2, 2024. Desig process underway.		
m17. Colonel Irvine School		New	Summer	Design and Specifications	100%	
Grades 5-9			2025	Construction Award	50%	
Added Capacity: 100				Construction Progress	0%	
				Note: Approved on August 2, 2024. Desig process underway.	n complete. Tender	
m18. Buffalo Rubbing Stone School	2	New	Summer	Design and Specifications	100%	
Grades K-5	_	11011	2025	Construction Award	50%	

<sup>\*</sup>Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.


Prepared by FES Page 5 of 6


# **CALGARY BOARD OF EDUCATION**

MODULAR CLASSROOM PROGRAM STATUS  March 18, 2025					
Building	Number of Units	Туре	Opening Date	Notes/Comments	
Added Capacity: 50				Construction Progress  Note: Approved on August 2, 2024. Design of process underway.	0% complete. Tender
M19. Kenneth D. Taylor School Grades K-6 Added Capacity: 50	2	New	Summer 2025	Design and Specifications  Construction Award  Construction Progress  Note: Approved on August 2, 2024. Design of process underway.	100% 50% 0% complete. Tender

Prepared by FES Page 6 of 6

<sup>\*</sup>Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.

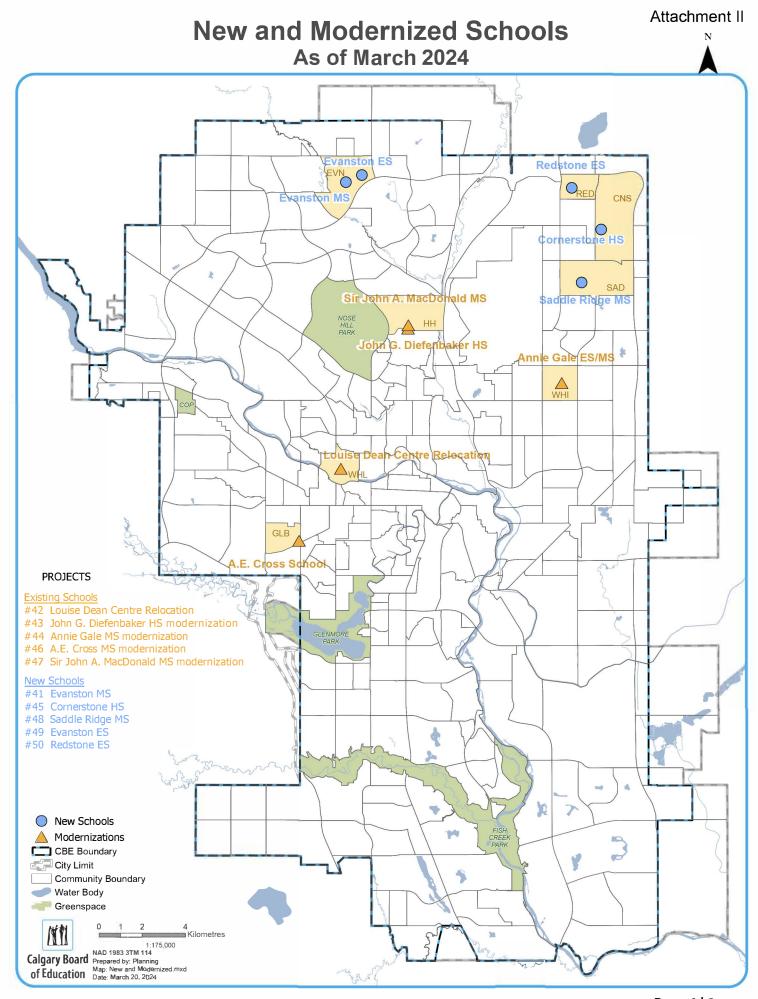

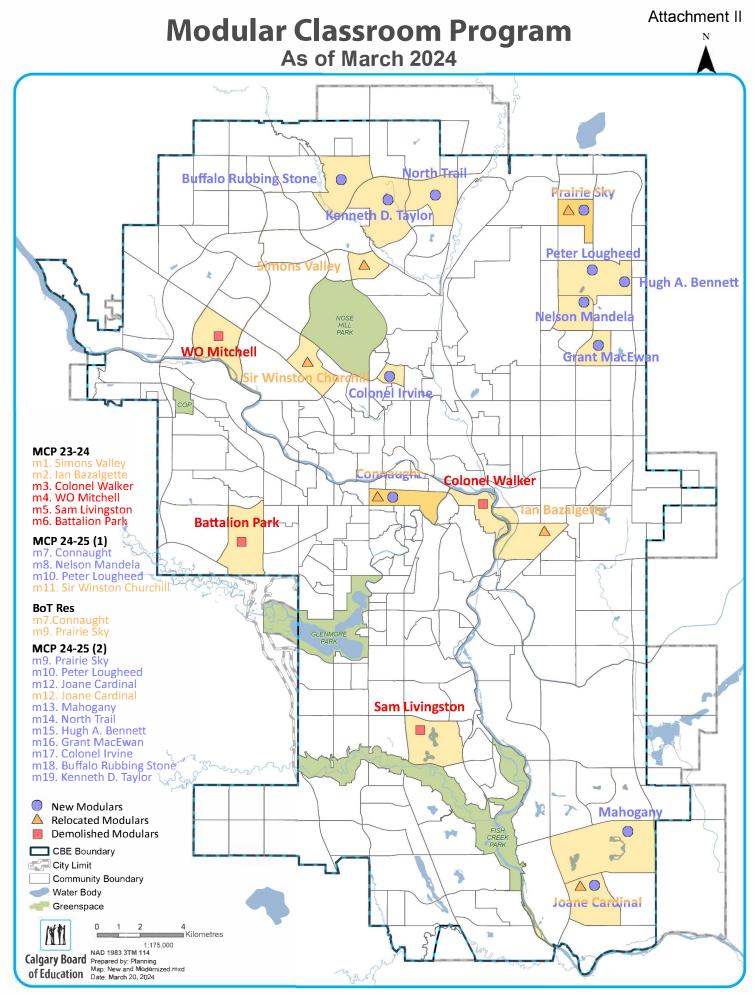

## Attachment III

### **Evanston middle school**





**Exterior Framing** 

**Structural Steel** 





**Building Envelope** 

**Structural Steel**
