

### **CBE Capital Projects Update**

Dec. 9, 2015

learning | as unique | as every student




#### **Our Mission and Values**

#### **Our Mission**

Each Student, in keeping with his or her individual gifts, will complete high school with a foundation of learning to function effectively in life, work and continued learning.


#### **Our Values**

- Students come first
- **Learning** is our central purpose
- Public education serves the common good



### Capital Projects Update

- CBE has 31 major capital projects well-underway:
  - 21 New schools
  - 3 Replacement schools
  - 6 Major modernizations
  - 1 Modular extension
- The target date for completion of these projects is between September 2016 and September 2018.

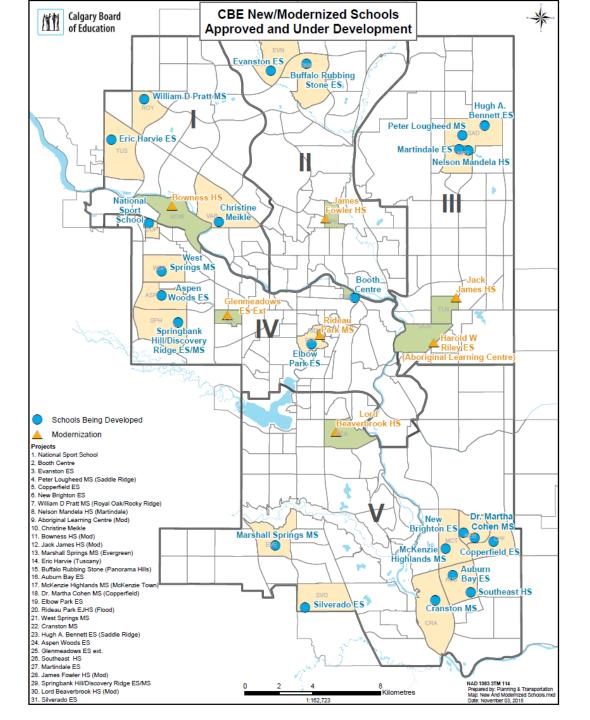

#### **School Names**

The Board of Trustees continues to announce new school names. The following schools have been named:

- Buffalo Rubbing Stone School (Buffalo Rubbing Stone School)
- Eric Harvie School (Tuscany)
- Hugh A. Bennett School (Saddle Ridge)
- Peter Lougheed School (Saddle Ridge)
- William D. Pratt School (Rocky Ridge/Royal Oak)
- Marshall Springs School (Evergreen)
- McKenzie Highlands School (McKenzie Towne)
- Dr. Martha Cohen School (New Brighton/Copperfield)
- Nelson Mandela High School (Northeast High School)

### Capital Projects Update (#3 to #7)

### **June 2014 Project Announcements**

- Construction is progressing at these sites:
  - Evanston Elementary School –behind schedule
  - Peter Lougheed Middle School on schedule
  - Copperfield Elementary School –behind schedule
  - New Brighton Elementary School on schedule
  - William D. Pratt Middle School on schedule

## Evanston School (#3)





# Peter Lougheed MS (Saddle Ridge) #4



## William D. Pratt MS (Royal Oak) #7



### Capital Projects Update (#8)

### **Nelson Mandela High School (NE Calgary)**


- Alberta Infrastructure is project managing the development
- Construction continues as scheduled
- A request for a gymnasium addition has been submitted to the Provincial Government

### Capital Projects Update (#9 and #10)

#### **January 2014 Project Announcements**

- Aboriginal Learning Centre (Harold W. Riley School)
   Construction is behind schedule. Structural steel erection has commenced. Block work progressing with gym 75% complete.
- Christine Meikle School Construction is on schedule.
   Roofing is in progress. Masonry work, steel stud and drywall are also progressing.

### Christine Meikle School (#10)

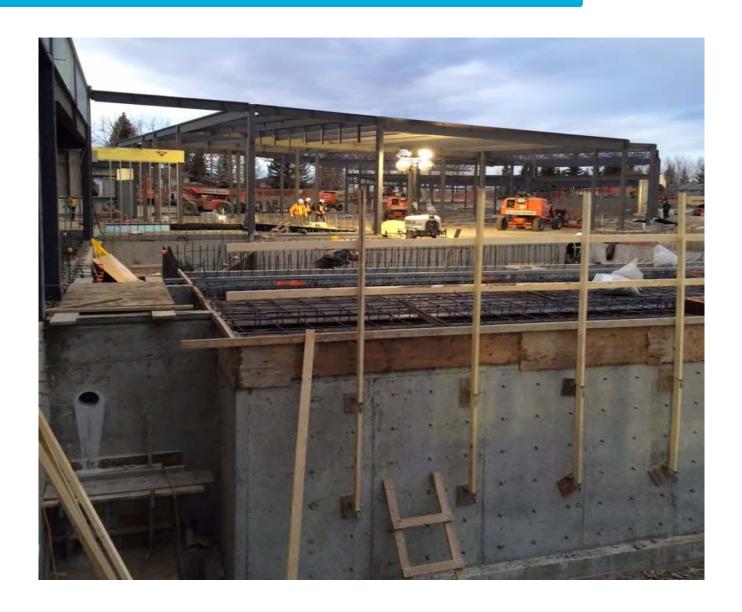

### Capital Projects Update (#11 & #12)

#### **January 2014 Project Announcements**

- Bowness HS Modernization Foundations are complete.
   Awaiting delivery of steel for erection. Construction progress is on schedule.
- Jack James HS Modernization Building trades expansion nearing completion for turnover in December 2015. Interior work progressing with mechanical and electrical installations. Greenhouse structural steel is complete.

### Capital Projects Update (#13 to #18)

#### **February 2014 Project Announcements**

- Eric Harvie ES, Buffalo Rubbing Stone ES, Auburn Bay
   ES Foundations are complete. Deep services utility
   connections are complete. Construction is behind
   schedule.
- Construction is progressing at McKenzie Highlands MS and Dr. Martha Cohen MS. Awaiting structural steel at both sites
- Construction has commenced at Marshall Springs MS, following receipt of required permits.

### McKenzie Highlands MS (#17)



### Dr. Martha Cohen MS (Copperfield) #18




### Capital Projects Update (#19 & #20)

#### **June 2013 Flood**

- Elbow Park ES The historic wall restraint work, together with all mass demolition activities has been completed.
   New foundations and concrete work have commenced.
   Construction is proceeding and is on schedule.
- Rideau Park EJHS The first phase design work for the mechanical systems move and new mechanical and electrical room scope is being developed.

## Elbow Park ES (#19)

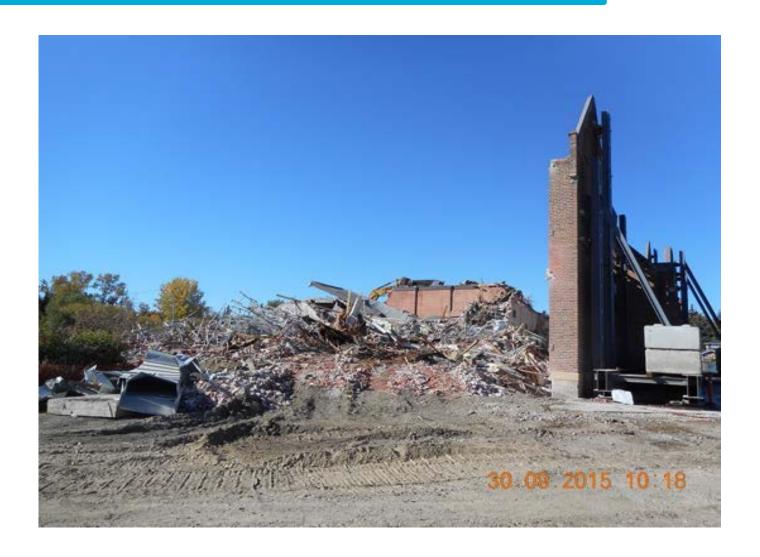

### Capital Projects Update (#21- #24)

#### **September 22, 2014 Project Announcements**

- Construction progress continues with slab and precast wall installation in progress at West Springs/Cougar Ridge MS and Cranston MS. Both projects are on schedule.
- Hugh A. Bennett ES and Dr. Roberta Bondar ES –
   Construction is slightly behind schedule on both projects.
   Awaiting a full building permit from the City.

### West Springs MS (#21)



### Cranston MS (#22)



### Hugh A Bennett ES (Saddle Ridge) #23



### Dr. Roberta Bondar ES (Aspen Woods) #24



### Capital Projects Update (#26)

### **September 22, 2014 Project Announcements**

- A schematic design concept has been developed for the Southeast Calgary HS
- The development permit application process has commenced with the pre-application planning process.

#### Capital Projects Update (#27, 29 & 31)

#### October 8, 2014 Project Announcements

- Martindale ES Working drawings and the pretender estimates are being reviewed by Alberta Infrastructure for tender release in January 2016.
- Springbank Hill/Discovery Ridge E/MS Working drawings are being prepared for Alberta Infrastructure review in January 2016 for a tender release in February 2016.
- Silverado School ES Working drawings and the pretender estimate are being reviewed by Alberta Infrastructure for a tender release in January 2016.

### Capital Projects Update (#28 & 30)

#### October 8, 2014 Project Announcements

 Steering committees have been set up and design development will commence immediately for both Lord Beaverbrook HS and James Fowler HS.



# Calgary Board of Education
